Six Month Meeting Minutes Summary

Oct 14, 2026 · @HAREEM

Overview

Eleven meetings took Lucky One and Lucky Core from a first conversation to a completed 6 month program, and in the illustrative results every target was met. This summary condenses the full Minutes of Meeting Register into one page of outcomes, decisions, actions and results. All figures are illustrative, and people appear by role.

No.	Date	Meeting	Key outcome
1	29 Oct 2026	Discovery call	Priorities confirmed: employees only, pilot cohort, measurable and private
2	5 Nov 2026	Proposal walkthrough	Proposal accepted in principle; costing questions raised
3	20 Nov 2026	Costing and agreement	Fee fixed at PKR 380,000; agreement signed
4	1 Dec 2026	Project kickoff	Roles, cohort, baseline survey and Masterclass 1 dates agreed
5	29 Dec 2026	Month 1 review	Baseline set; shift clash solved with a written summary
6	26 Jan 2027	Month 2 progress	Energy up; Masterclass 3 moved before Ramadan
7	2 Feb 2027	Ramadan planning	Fasting month tracking and tip timing agreed
8	30 Mar 2027	Month 4 midpoint review	Targets on track; cafeteria choice guide agreed
9	27 Apr 2027	Month 5 review	Endline survey and Masterclass 6 dates set around Eid
10	25 May 2027	Final impact review	Report accepted; targets met in the illustrative results

No.	Date	Meeting	Key outcome
11	28 May 2027	Close out and expansion	Expansion options and archiving agreed

Key Decisions

Seven decisions shaped the program, and none was reversed during the six months.

Theme	Decision	Meeting
Scope and audience	Employees only, a pilot cohort of about 60 participants, voluntary participation	1, 4
Fee and payment	Fixed fee of PKR 380,000 in four milestones of PKR 95,000, with extras only on written approval	3
Schedule	Baseline 7 to 11 December; masterclasses on 15 Dec, 19 Jan, 4 Feb, 23 Mar, 20 Apr and 13 May	4, 5, 6, 9
Privacy	Individual data stays with Hareem Fatima; HR receives anonymised group results	1, 4
Ramadan	Masterclass 3 before Ramadan; logs about sehri and iftar; tips posted at 7:30 PM	6, 7
Cafeteria	A one page choice guide, with HR raising it with the cafeteria operator	8
After the pilot	A scale up option with costing, reviewed by HR	11

Action Items Tracker

All actions through the final review were completed, and three follow up actions remain open.

Action	Owner	Due	Status
Send bid and proposal	Hareem Fatima	2 and 4 Nov 2026	Completed


Action	Owner	Due	Status
Send costing details	Hareem Fatima	9 Nov 2026	Completed
Process first milestone of PKR 95,000	Finance contact	27 Nov 2026	Completed
Run baseline survey	Hareem Fatima and HR Manager	7 to 11 Dec 2026	Completed
Send Month 2 dashboard	Hareem Fatima	25 Jan 2027	Completed
Prepare Ramadan energy guide	Hareem Fatima	3 Feb 2027	Completed
Prepare cafeteria choice guide	Hareem Fatima	9 Apr 2027	Completed
Run endline survey	Hareem Fatima and HR Manager	14 to 20 May 2027	Completed
Send expansion option with costing	Hareem Fatima	4 Jun 2027	Open
Share summary with leadership	Head of HR	4 Jun 2027	Open
Archive the WhatsApp groups	Hareem Fatima	27 Jun 2027	Open

Progress Against Targets

All five targets were met in the illustrative results, with afternoon energy improving every month.

Afternoon energy rose from 5.2 to 7.2 out of 10, beating the 30% target

Average afternoon energy score, pilot cohort, illustrative figures

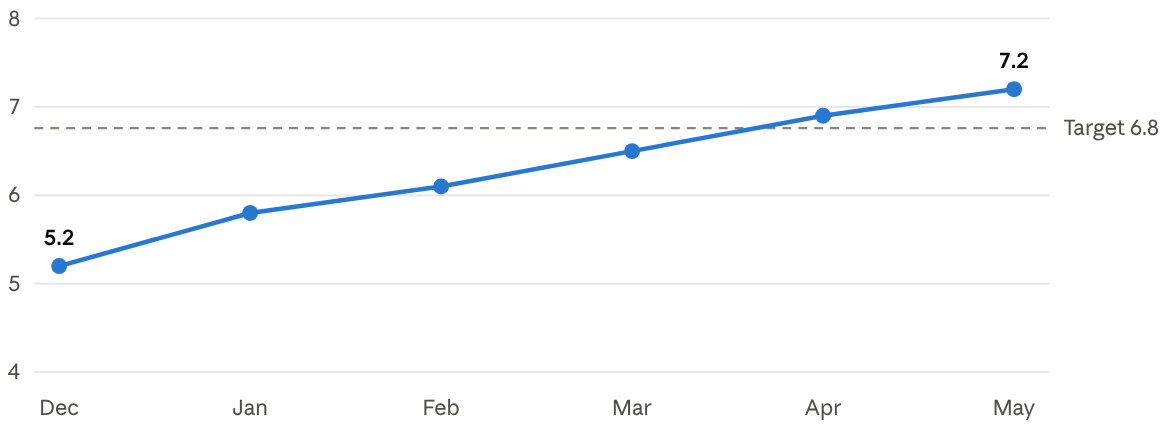

December is the baseline. The dashed line marks a 30% improvement on the baseline.

illustrative sample figures, December 2026 to May 2027

Target	Goal	Result	Status
Afternoon energy score	30% improvement	5.2 to 7.2 out of 10 (38%)	Met
Post lunch focus score	25% improvement	5.4 to 7.0 out of 10 (30%)	Met
Daily logging	60% of active participants on 4 or more days a week	72%	Met
Masterclass attendance	At least 75%	87.5% average	Met
Satisfaction	At least 80%	91% (4.55 out of 5 average)	Met

Lessons Learned and Next Steps

The program worked because it was short, voluntary, fitted to shifts and reported openly.

Lessons learned

1. Plan around shift handovers early and offer a written summary or a repeat session.

2. Short daily logs of under two minutes kept participation above target, even during Ramadan.
3. Employees want practical links to what they actually eat, so the cafeteria choice guide was valuable.
4. Honest reporting builds trust: limited absenteeism data was stated as such.

Recommended next steps

1. HR reviews the scale up option, which could add a second cohort, other sites or a quarterly refresher masterclass.
2. HR shares the summary with senior leadership by 4 June 2027.
3. Hareem Fatima sends the expansion costing by 4 June 2027 and archives the WhatsApp groups on 27 June 2027.
